

# SCoREBOARD

## Corporate Actions – H2 2021

### Greek NSG

The Single Collateral Management Rulebook for Europe (SCoRE) contains 15 Standards related to the processing of corporate actions (published as the [SCoRE Standards for Corporate Actions](#)). Implementation progress is monitored twice per year. This summary report presents the results of the H2 2021 monitoring exercise conducted by the Greek NSG with the involvement of the following stakeholders:

- 2 CSDs – ATHEXCSD, BOGS
- 7 Custodians
- 2 Issuers

11 entities are monitored in the Greek market

The SCoRE Overview provides a high-level summary of the H2 2021 monitoring exercise.

 <small>GREEK COLLATERAL MANAGEMENT RULEBOOK FOR EUROPE</small>	 <b>Response Rate</b>	 <b>Implementation Status</b>	 <b>Milestone achieved?</b>	 <b>Implemented on Time?</b>
Custodians	100%	Implemented 26.1% Analysis started 46.3% Implementation started 12.3%	57%	100%
Issuers	100%	Yes 85% No 15%	n/a	n/a
CSD - AthexCSD	100%	Implemented 5.08% Analysis started 39.4% Implementation started 44.4%	No	Yes

Note: Implemented on time reflects the entity's expected ability to achieve the final milestone on time.

This NSG summary report is structured as follows: The Executive Summary provides an overview of the responses received per Entity Type i.e. CSD, TPA, Custodian etc. Section 1 presents the compliance status of each entity type. Section 2 provides an overview of the progress against the individual milestones. Section 3 then provides a

more detailed overview of the implementation status per Standard for each entity type.

## Executive Summary

A very high response rate has been achieved amongst the Greek community for this monitoring cycle

The response rate of the Greek community to the H2 2021 monitoring cycle for the implementation of the SCoRE Corporate Actions Standards was very high, i.e. all monitored actors filled the relevant questionnaires. According to the replies received, the implementation of the standards in the Greek market is on track. For additional information, please refer to the below analysis of the responses per entity type.

### CSD – ATHEXCSD

ATHEXCSD has participated in the current reporting cycle and expects to meet the final milestones on time

The ATHEXCSD, the CSD in Greece managing equities and a limited amount of corporate bonds has reported that all Corporate Actions Standards applicable to its activities will be implemented.

Regarding the milestones and according to the reporting provided, some of them are expected to be delayed. In any case, the final milestones will be met.

Following the above, it is considered that, there are no issues of concern regarding the compliance of the ATHEXCSD to the Corporate Actions Standards and the CSD will most likely be compliant with the standards by November 2023.

### CSD – BOGS

BOGS has commenced its analysis and expects to meet almost all milestones on time

BOGS, the CSD in Greece managing the Government bonds, has reported that it will implement all the standards applicable to its activities. BOGS has indicated that analysis for some of the standards is still a work in progress and a minor delay referring to the start of the implementation of the required updates in its system is expected. However, this will not affect the remaining milestones until the final one that will be met according to the relevant timeline. Therefore this CSD is expected to be compliant with the standards by November 2023.

### Custodians

Custodians have fully participated in this reporting round and they are expected to meet the final milestone on time

Custodians in the Greek market have fully participated in this reporting round by indicating the current status for each one of the standards that are applicable to their activities. Following their replies, the relevant standards are either already implemented, via their existing processes or internal analysis/implementation has started. The majority of the custodians have also confirmed that they will be able to meet the relevant milestones on time, while a minority of them is not expected to meet on time all the milestones but in any case, they will be ready for the go-live of the standards.

## **Issuers**

Issuer awareness is very high

Regarding the monitored issuers awareness of their obligations stemming from the Corporate Actions Standards, a percentage of 85% has been reported.

## **NCB**

Bank of Greece is on track to adopt the SCoRE Standards in November 2023

Bank of Greece is on track to implement the Corporate Actions Standards for its collateral management activities in November 2023.

## SCoREBOARD

This section presents the overall compliance status in the market. CSDs and TPAs are monitored on an individual basis and are assigned a colour-code status in accordance with the methodology outlined in Box 1<sup>1</sup>. Custodians and Issuers are monitored on an aggregated basis and assigned a percentage compliance status.

### Box 1

#### SCoREBOARD – Implementation Phase

---



- The Standard has been implemented
- Implementation of the Standard is on schedule (based on the agreed milestones)
- Implementation is behind schedule (based on the agreed milestones)
- Implementation has not started

---

For custodians and issuers, progress is monitored and reported as a percentage; for example the % of custodians in a given market who have started internal adaptation of IT systems.

---

<sup>1</sup> For further details please refer to the [AMI-SeCo Monitoring Framework](#)

**Table A**  
**SCoREBOARD**

STANDARD	Custodians	Issuers	CSD - AthexCSD	CSD - BOGS
1A: Notification	100%	60%	G	Y
1B: Instruction	100%		G	Y
1C: Advise	100%		G	Y
1D: Confirmation	98%		G	Y
1E: Reversal	74%		G	Y
1F: Meeting Notification	100%	44%	G	Y
1G: Meeting Instruction	100%		G	N/A
1H: Meeting Results	97%		Y	N/A
2: Calculation of Proceeds	87%	50%	G	Y
3: Consistency of Information	86%	50%	G	Y
4: Rounding Rule 1	86%	100%	Y	Y
4: Rounding Rule 2	100%	100%	B	B
4: Rounding Rule 3	100%	100%	B	B
4: Rounding Rule 4	71%	100%	Y	Y
4: Rounding Rule 5	100%	100%	B	Y
5: Negative Cash Flows	71%	50%	Y	B
6: Business Day Rule		50%	Y	B
7: Securities Amount Data Rule 1		50%	Y	B
7: Securities Amount Data Rule 2		50%	B	N/A
7: Securities Amount Data Rule 3		50%	B	N/A
7: Securities Amount Data Rule 4		50%	B	N/A
8: Payment Time Rule 1		100%	B	B
8: Payment Time Rule 2		100%	B	B
8: Payment Time General Principle 3		50%	N/A	B
9: Processing Status	86%	100%	G	Y
10: Blocking Rule 1	86%		G	B
10: Blocking Rule 2	71%		G	N/A
10: Blocking Rule 3	86%		G	N/A
10: Blocking Rule 4	100%		G	Y
10: Blocking Rule 5	86%		G	N/A
11: Default Option	100%	100%	B	Y
12: Handling of Fees	86%		Y	N/A
13: Reversal	86%	100%	G	Y
14: Foreign Currency			B	N/A
15: ISO 20022 Messaging	62%		Y	Y

Notes:

- For CSDs and TPAs the colour-code reflects the current implementation status of each Standard in accordance with the methodology outlined in Box 1 above.
- TPAs are using custody services provided by CSDs or Custodians in order to disseminate CA information to Collateral Givers and Collateral Takers. Monitoring of TPAs thus focuses on the implementation of triparty specific workflows described in Standard 1.
- For custodians the % indicates that the standard has either already been implemented, or that implementation is on track i.e. at a minimum that analysis has already started or that implementation has started per Standard.
- Issuers were asked to confirm awareness of their obligation to provide all relevant information to the Issuer CSD (on a Yes/No basis). The % reflects the number of issuers who responded yes to the survey
- Percentages are calculated on the basis of expected respondents, i.e. number of entities monitored in the market.
- A plausibility check was performed by the CMH-TF secretariat.

## 2 Milestones

This section tracks an entity's progress in implementing the Standards on an ongoing basis. 13 milestones have been defined as listed in the box below.

### Box 2

#### SCoRE Milestones

Milestone	Description	Date
<b>M1</b>	<b>Analysis Started:</b> Have you commenced an in-depth analysis of all applicable SCoRE Standards in order to identify and document all the changes required to internal processes and procedures in order to comply with the SCoRE Standards?	<b>30/06/2020</b>
<b>M2</b>	<b>Initial Communication:</b> Has initial high-level communication with external stakeholders on the changes introduced by SCoRE commenced?	<b>01/03/2021</b>
<b>M3</b>	<b>Analysis Completed:</b> Have you completed an in-depth analysis of all applicable SCoRE Standards?	<b>31/07/2021</b>
<b>M4</b>	<b>Documentation Completed:</b> Have you documented all the internal processes and procedures which need to be adapted in order to comply with the SCoRE Standards?	<b>31/12/2021</b>
<b>M5</b>	<b>Detailed External Communication:</b> Has detailed communication started regarding (i) upcoming changes in business processes, (ii) messaging formats and usage guidelines (in the case of new messages based on non-registered latest drafts by SWIFT) and (iii) planned testing activities been provided to users?	<b>31/12/2021</b>
<b>M6</b>	<b>SCoRE Adaptation Started:</b> Have you started to adapt/develop the processes and procedures in order to comply with the SCoRE Standards?	<b>01/01/2022</b>
<b>M7</b>	<b>SCoRE Adaptation Complete:</b> Have you completed the necessary adaptations/developments for the processes and procedures in order to comply with the SCoRE Standards?	<b>30/06/2022</b>
<b>M8</b>	<b>Internal Testing Started for SCoRE:</b> Have you started to test the changes to your internal processes and procedures which have been introduced in order to comply with the SCoRE Standards?	<b>01/07/2022</b>
<b>M9</b>	<b>Internal Testing Complete for SCoRE:</b> Have you completed the necessary internal testing?	<b>02/12/2022</b>
<b>M10</b>	<b>External Testing Started for SCoRE:</b> Are you in a position to test the changes introduced in order to comply with the SCoRE Standards with your user community (i.e. CSD participants / Collateral Givers and Collateral Takers in the context of the Standards applicable to TPAs)?	<b>05/12/2022</b>
<b>M11</b>	<b>Final External Communication on SCoRE:</b> has final communication to users been provided (i.e. updated user guide to reflect the changes implemented, final message usage guidelines for A2A communication) related to the SCoRE Standards?	<b>01/04/2023</b>
<b>M12</b>	<b>External Testing Completed for SCoRE:</b> Is the testing of the changes introduced in order to comply with the SCoRE Standards with your user community completed (i.e. CSD participants / Collateral Givers and Collateral Takers in the context of the Standards applicable to TPAs)?	<b>13/10/2023</b>
<b>M13</b>	<b>SCoRE Standards Implemented:</b> have the SCoRE Standards been implemented?	<b>20/11/2023</b>

Notes: N/A

Milestones expected to be achieved in the current reporting period are highlighted in blue in the header of Table B below. The blue colour-code is then assigned to those milestones which have been successfully achieved to date for each respective entity. Milestones which will only be achieved later are assigned a yellow status, while milestones which will only be achieved with significant delays / where work has not yet commenced are marked in red.

For the remaining milestones (i.e. milestones due to be achieved only after the current reporting cycle) the colour-code indicates an entity's expected ability to achieve a future milestone on time. The expected date of achievement is also indicated in the table if it is different to the milestone date defined by AMI-SeCo.

**Table B**  
Milestones

	Custodians	CSD - AthexCSD	CSD - BOGS
Milestone 1 June 2020	43%	07/21	Yes
Milestone 2 March 2021	57%	Yes	Yes
Milestone 3 July 2021	57%	06/22	Yes
Milestone 4 December 2021	57%	07/22	Yes
Milestone 5 December 2021	71%	08/22	Yes
Milestone 6 January 2022	43%	07/22	03/22
Milestone 7 June 2022	43%	12/22	Yes
Milestone 8 July 2022	43%	01/23	Yes
Milestone 9 December 2022	71%	04/23	Yes
Milestone 10 December 2022	71%	03/23	Yes
Milestone 11 April 2023	86%	Yes	Yes
Milestone 12 October 2023	100%	Yes	Yes
Milestone 13 November 2023	100%	Yes	Yes

Notes: Actors were asked to report for all milestones, i.e. whether they meet the current milestones and whether they expect to meet the dates for future milestones.

### Summary

As shown in the above table, BOGS is on track and it has confirmed that it will meet all milestones on time, excluding M6 relating to the start of the adaptation of its system. However, this is not expected to be an issue for the timely implementation of the standards, as the remaining milestones are expected to be met on time. ATHEXCSD has also indicated that although some delays are foreseen for the interim milestones, the final ones are expected to be met according to the existing timeframe. As far as the custodians are concerned, while for some of them delays in the interim milestones have been reported, all of them have confirmed that the final milestones will be met in the foreseen timeline.


### 3

## Implementation status per SCoRE Standard

This section presents the implementation status of each Standard per entity type.

### CSD – ATHEXCSD

#### Implementation status per SCoRE Standard

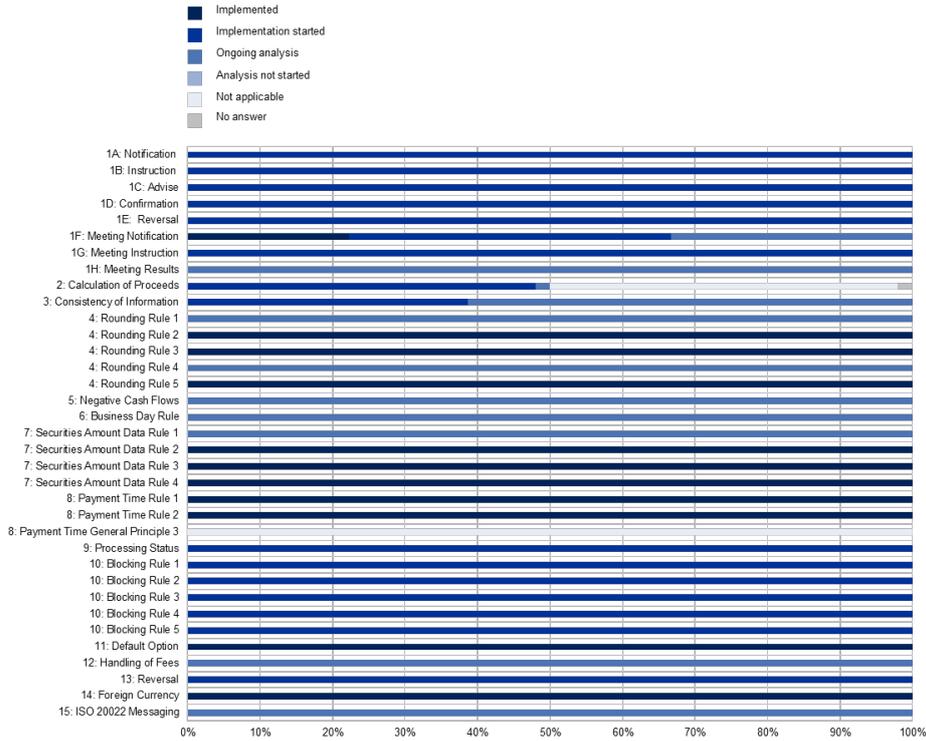


#### Notes

N/A

## CSD – BOGS

### Implementation status per SCoRE Standard

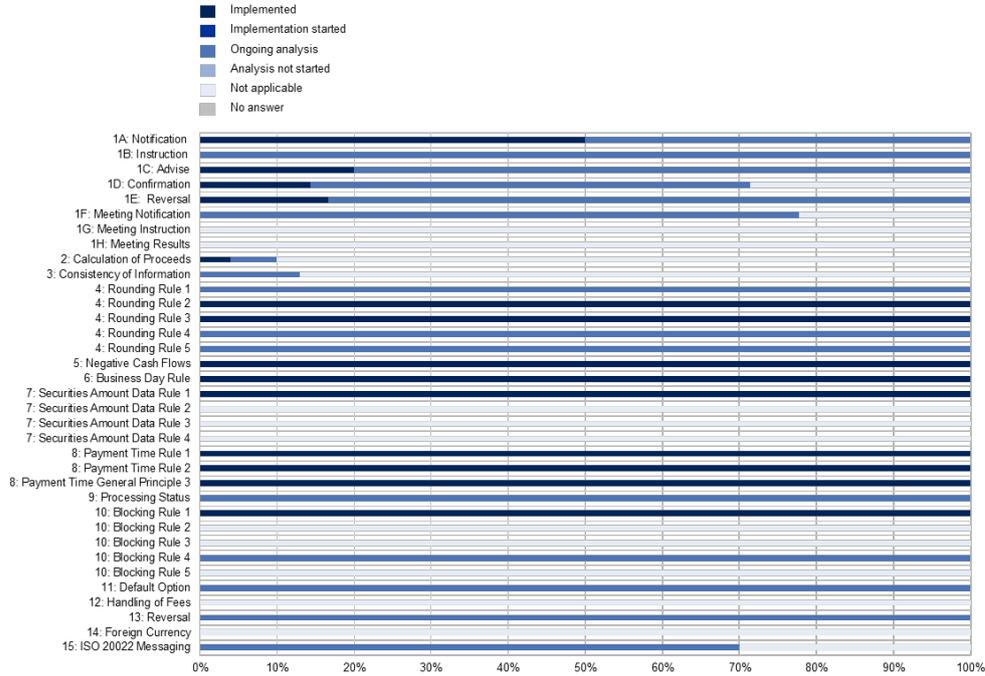


#### Notes

A plausibility check was performed by the CMH-TF secretariat.

## Custodians

### Implementation status per SCoRE Standard

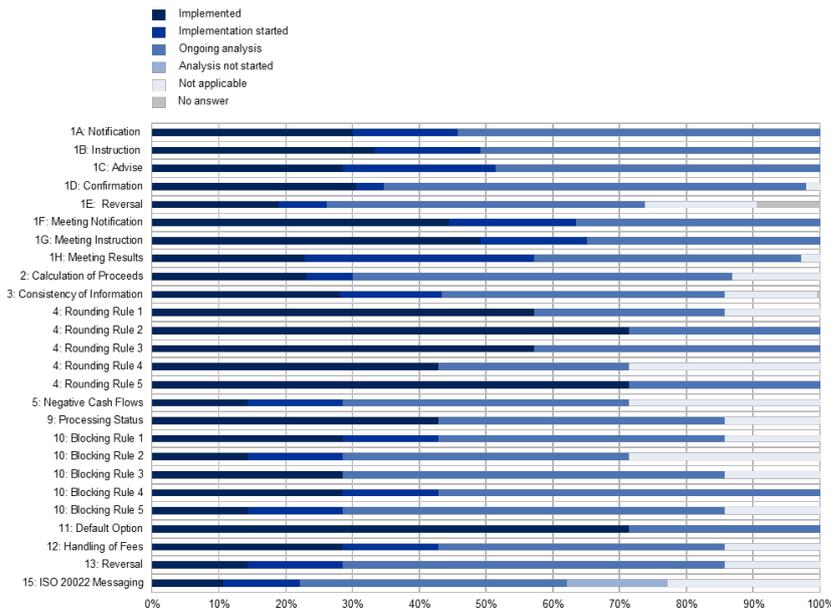


#### Notes

N/A

## Issuers

### Fulfilment of obligations per SCoRE Standard

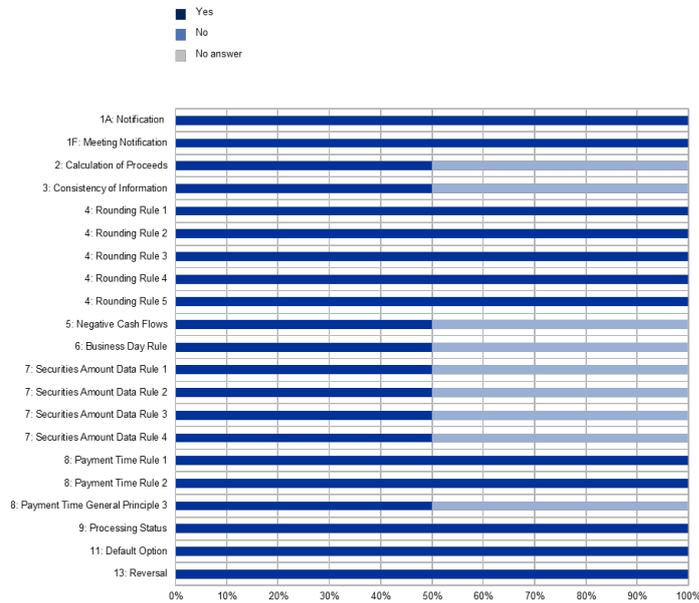

#### Notes

N/A

© European Central Bank, 2022

Postal address 60640 Frankfurt am Main, Germany

Telephone +49 69 1344 0

Website [www.ecb.europa.eu](http://www.ecb.europa.eu)

All rights reserved. Reproduction for educational and non-commercial purposes is permitted provided that the source is acknowledged.

The cut-off date for the data included in this report was 17 November 2021.

For specific terminology please refer to the [ECB glossary](#) (available in English only).
