

# SCoREBOARD

## Corporate Actions – H1 2021

### Portuguese NSG

The Single Collateral Management Rulebook for Europe (SCoRE) contains 15 Standards related to the processing of corporate actions (published as the [AMI-SeCo Standards for Corporate Actions](#)). Implementation progress is monitored twice per year. This summary report presents the results of the H1 2021 monitoring exercise conducted by the Portuguese NSG with the involvement of the following stakeholders:

- 1 CSD – Interbolsa
- 9 Custodians
- 1 Issuer and 1 Issuer Association

12 entities are monitored in the Portuguese market

The SCoRE Overview provides a high-level summary of the H121 monitoring exercise.

### SCoRE Overview

 <small>SINGLE COLLATERAL MANAGEMENT RULEBOOK FOR EUROPE</small>	 <b>Response Rate</b>	 <b>Implementation Status</b>	 <b>Milestones achieved?</b>	 <b>Implemented on Time?</b>
Custodians	89%	Implemented 30.8% Analysis started 14.5% Implementation started 186%	39%	89%
Issuers	100%	Yes 48% No 52%	n/a	n/a
CSD - Interbolsa	100%	Implemented 10.5% Analysis started 34.7% Implementation started 0%	No	Yes

Note: Implemented on Time reflects the entity's ability to meet the final reporting milestone prior to the adoption of the Standards.

This NSG summary report is structured as follows: The Executive Summary provides an overview of the responses received per Entity Type i.e. CSD, TPA, Custodian etc. Section 1 presents the compliance status of each entity type. Section 2 provides an overview of the progress against the individual milestones. Section 3 then provides a more detailed overview of the implementation status per Standard for each entity type.

## Executive Summary

Implementation of the Corporate Action Standards in the Portuguese market is on track

Implementation of the Corporate Action Standards in the Portuguese market is on track.

The majority of the reporting entities responded to the survey and revealed a high level of compliance.

This section presents the key findings of the survey for each entity type.

### CSD – Interbolsa

Interbolsa implementation is on track

Interbolsa is fully compliant with 11% of the standards already implemented (14% if not applicable it is not considered) and 35% of the standards are already in the stage of ongoing analysis.

Interbolsa reported a delay in milestones 2 and 3, but it is expected that the implementation date of November 2023 will be met.

### Custodians

Portuguese custodians already have a significant percentage of standards implemented

Portuguese custodians have already implemented a significant percentage of standards (31%). The analysis has started for another 15% of the standards and for 2% the implementation has started.

### Issuers

48% of the Issuers answers confirm awareness of obligation

Almost half of the answers confirm awareness of obligation from the issuers.

For the time being, only one standard (1F: Meeting Notification) needs to be highlighted with low compliance.

Nevertheless, looking to the Issuer Association answers (representing the main Portuguese issuers) we have only 24% of awareness of obligation.

### NCB

Banco de Portugal is on track to adopt the AMI-SeCo Standards in November 2023

Banco de Portugal is on track to implement the AMI-SeCo Standards for Corporate Actions for its collateral management activities by November 2023.

## SCoREBOARD

This section presents the overall compliance status in the market. CSDs and TPAs are monitored on an individual basis and are assigned a colour-code status in accordance with the methodology outlined in Box 1<sup>1</sup>. Custodians and Issuers are monitored on an aggregated basis and assigned a percentage compliance status.

### Box 1

#### SCoREBOARD – Implementation Phase

---



- The Standard has been implemented
- Implementation of the Standard is on schedule (based on the agreed milestones)
- Implementation is behind schedule (based on the agreed milestones)
- Implementation has not started

---

For custodians and issuers, progress is monitored and reported as a percentage; for example the % of custodians in a given market who have started internal adaptation of IT systems.

---

<sup>1</sup> For further details please refer to the [AMI-SeCo Monitoring Framework](#)

**Table A**  
**SCoREBOARD**

STANDARD	Custodians	Issuers	CSD - Interbolsa
1A: Notification	56%	42%	G
1B: Instruction	64%		G
1C: Advise	56%		G
1D: Confirmation	60%		G
1E: Reversal	56%		G
1F: Meeting Notification	67%	0%	G
1G: Meeting Instruction	58%		N/A
1H: Meeting Results	56%		N/A
2: Calculation of Proceeds	53%	50%	G
3: Consistency of Information	43%	50%	G
4: Rounding Rule 1	56%	50%	G
4: Rounding Rule 2	78%	100%	B
4: Rounding Rule 3	67%	50%	B
4: Rounding Rule 4	78%	50%	B
5: Negative Cash Flows	22%	50%	B
6: Business Day Rule		50%	G
7: Securities Amount Data		100%	B
8: Payment Time Rule 1		50%	G
8: Payment Time Rule 2		100%	B
8: Payment Time Rule 3		100%	G
9: Processing Status	67%	50%	G
10: Blocking	56%		G
11: Default Option	67%	50%	G
12: Handling of Fees	44%		N/A
13: Reversal	67%	50%	G
14: Foreign Currency			B
15: ISO 20022 Messaging	34%		Y

Notes:

- For CSDs and TPAs the colour-code reflects the current implementation status of each Standard in accordance with the methodology outlined in Box 1 above.
- TPAs are using custody services provided by CSDs or Custodians in order to disseminate CA information to Collateral Givers and Collateral Takers. Monitoring of TPAs thus focuses on the implementation of triparty specific workflows described in Standard 1.
- For custodians the % indicates that the standard has either already been implemented, or that implementation is on track i.e. at a minimum that analysis has already started or that implementation has started per Standard.
- Issuers were asked to confirm awareness of their obligation to provide all relevant information to the Issuer CSD (on a Yes/No basis). The % reflects the number of issuers who responded yes to the survey
- Percentages are calculated on the basis of expected respondents, i.e. number of entities monitored in the market.

## 2 Milestones

This section tracks an entity's progress in implementing the Standards on an ongoing basis. 13 milestones have been defined as listed in the box below.

### Box 2 SCoRE Milestones

Milestone	Description	Date
M1	<b>Analysis Started:</b> Have you commenced an in-depth analysis of all applicable SCoRE Standards in order to identify and document all the changes required to internal processes and procedures in order to comply with the SCoRE Standards?	30/06/2020
M2	<b>Initial Communication:</b> Has initial high-level communication with external stakeholders on the changes introduced by SCoRE commenced?	01/03/2021
M3	<b>Analysis Completed:</b> Have you completed an in-depth analysis of all applicable SCoRE Standards?	31/07/2021
M4	<b>Documentation Completed:</b> Have you documented all the internal processes and procedures which need to be adapted in order to comply with the SCoRE Standards?	31/12/2021
M5	<b>Detailed External Communication:</b> Has detailed communication started regarding (i) upcoming changes in business processes, (ii) messaging formats and usage guidelines (in the case of new messages based on non-registered latest drafts by SWIFT) and (iii) planned testing activities been provided to users?	31/12/2021
M6	<b>SCoRE Adaptation Started:</b> Have you started to adapt/develop the processes and procedures in order to comply with the SCoRE Standards?	01/01/2022
M7	<b>SCoRE Adaptation Complete:</b> Have you completed the necessary adaptations/developments for the processes and procedures in order to comply with the SCoRE Standards?	30/06/2022
M8	<b>Internal Testing Started for SCoRE:</b> Have you started to test the changes to your internal processes and procedures which have been introduced in order to comply with the SCoRE Standards?	01/07/2022
M9	<b>Internal Testing Complete for SCoRE:</b> Have you completed the necessary internal testing?	02/12/2022
M10	<b>External Testing Started for SCoRE:</b> Are you in a position to test the changes introduced in order to comply with the SCoRE Standards with your user community (i.e. CSD participants / Collateral Givers and Collateral Takers in the context of the Standards applicable to TPAs)?	05/12/2022
M11	<b>Final External Communication on SCoRE:</b> has final communication to users been provided (i.e. updated user guide to reflect the changes implemented, final message usage guidelines for A2A communication) related to the SCoRE Standards?	01/04/2023
M12	<b>External Testing Completed for SCoRE:</b> Is the testing of the changes introduced in order to comply with the SCoRE Standards with your user community completed (i.e. CSD participants / Collateral Givers and Collateral Takers in the context of the Standards applicable to TPAs)?	13/10/2023
M13	<b>SCoRE Standards Implemented:</b> have the SCoRE Standards been implemented?	20/11/2023

Notes: N/A

Milestones expected to be achieved in the current reporting period are highlighted in blue in the header of Table B below. The blue colour-code is then assigned to those milestones which have been successfully achieved to date for each respective entity. Milestones which will only be achieved later are assigned a yellow status, while milestones which will only be achieved with significant delays / where work has not yet commenced are marked in red.

For the remaining milestones (i.e. milestones due to be achieved only after the current reporting cycle) the colour-code indicates an entity's expected ability to achieve a future milestone on time. The expected date of achievement is also indicated in the table if it is different to the milestone date defined by AMI-SeCo.

**Table B**  
Milestones

	Custodians	CSD - Interbolsa
Milestone 1 June 2020	33%	Yes
Milestone 2 March 2021	44%	06/21
Milestone 3 July 2021	44%	12/21
Milestone 4 December 2021	67%	Yes
Milestone 5 December 2021	67%	Yes
Milestone 6 January 2022	33%	Yes
Milestone 7 June 2022	44%	Yes
Milestone 8 July 2022	44%	Yes
Milestone 9 December 2022	56%	01/23
Milestone 10 December 2022	56%	Yes
Milestone 11 April 2023	78%	Yes
Milestone 12 October 2023	89%	Yes
Milestone 13 November 2023	89%	Yes

Notes: Actors were asked to report for all milestones, i.e. whether they meet the current milestones and whether they expect to meet the dates for future milestones.


### Summary

## 3 In general PT-NSG participants do not anticipate problems to achieve the SCoRE milestones. Implementation status per AMI-SeCo Standard

This section presents the implementation status of each Standard per entity type.

## CSD – Interbolsa


### Implementation status per AMI-SeCo Standard

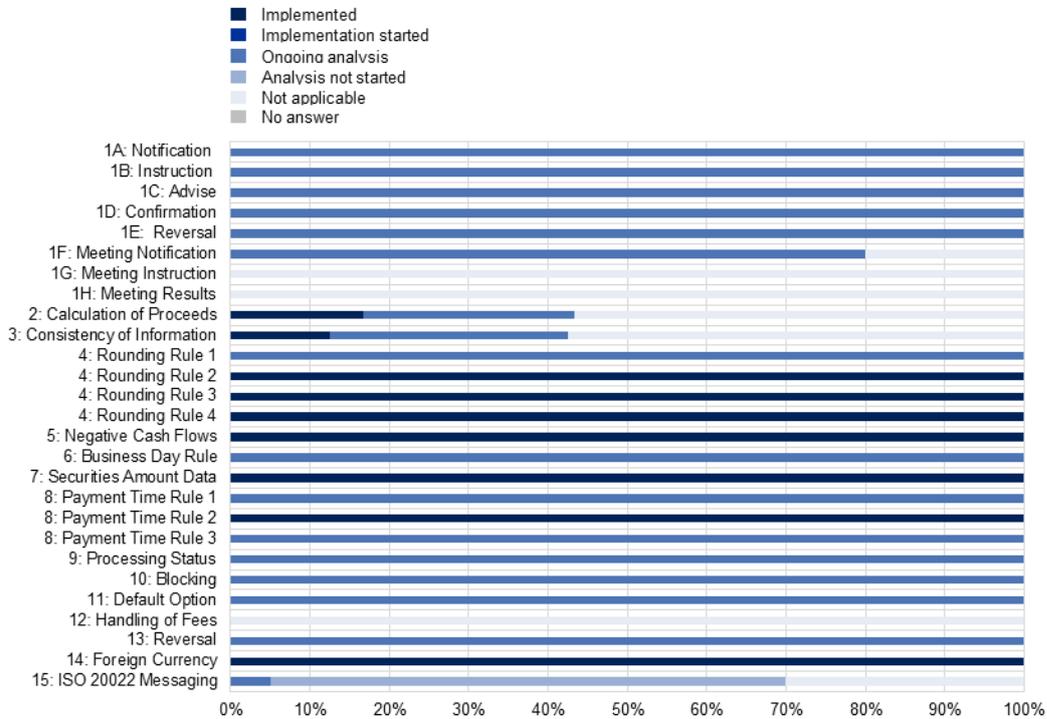

Notes  
N/A

## Custodians


### Implementation status per AMI-SeCo Standard

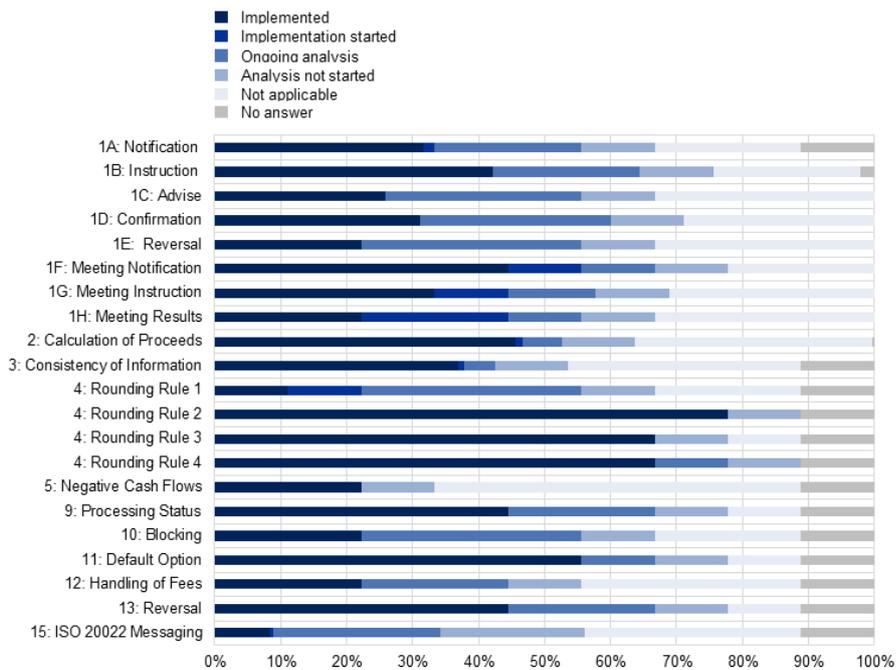

Notes  
N/A

## Issuers

### Fulfilment of obligations per AMI-SeCo Standard

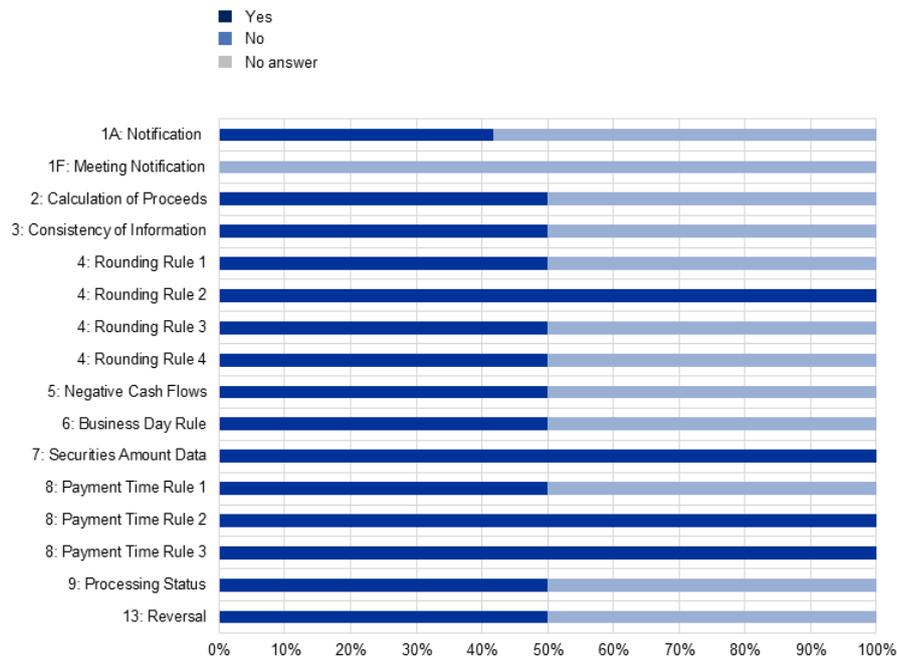

#### Notes

N/A

#### © European Central Bank, 2021

Postal address 60640 Frankfurt am Main, Germany  
Telephone +49 69 1344 0  
Website [www.ecb.europa.eu](http://www.ecb.europa.eu)

All rights reserved. Reproduction for educational and non-commercial purposes is permitted provided that the source is acknowledged.

The cut-off date for the data included in this report was 21 May 2021.

For specific terminology please refer to the [ECB glossary](#) (available in English only).
