



EUROPEAN CENTRAL BANK

EUROSYSTEM

T2-T2S Consolidation Community Readiness

European Central Bank

A large, semi-transparent globe is centered on the right side of the slide. The globe is surrounded by several white orbital lines with small white dots at their intersections. The 'target' logo is overlaid on the globe in a blue, lowercase, sans-serif font. Below the 'target' text, the word 'services' is written in a smaller, orange, lowercase, sans-serif font.

target
services

23/01/2020

Mayte Arráez
Deputy Head of Market Infrastructures Support division
Market Infrastructure and Payments

Community Readiness



1,056 Direct participants
659 Indirect participants


85 Ancillary systems

346,834 payments
daily average

Source: TARGET Annual report
TARGET2 transfers based on the
originator and final beneficiary
banks' locations
[https://www.ecb.europa.eu/pub/pdf/t
argetar/ecb.targetar2018.en.pdf](https://www.ecb.europa.eu/pub/pdf/targetar/ecb.targetar2018.en.pdf)

Overall key milestones for T2 participants


The Community Readiness Reporting tracks the progress on the overall key milestones.

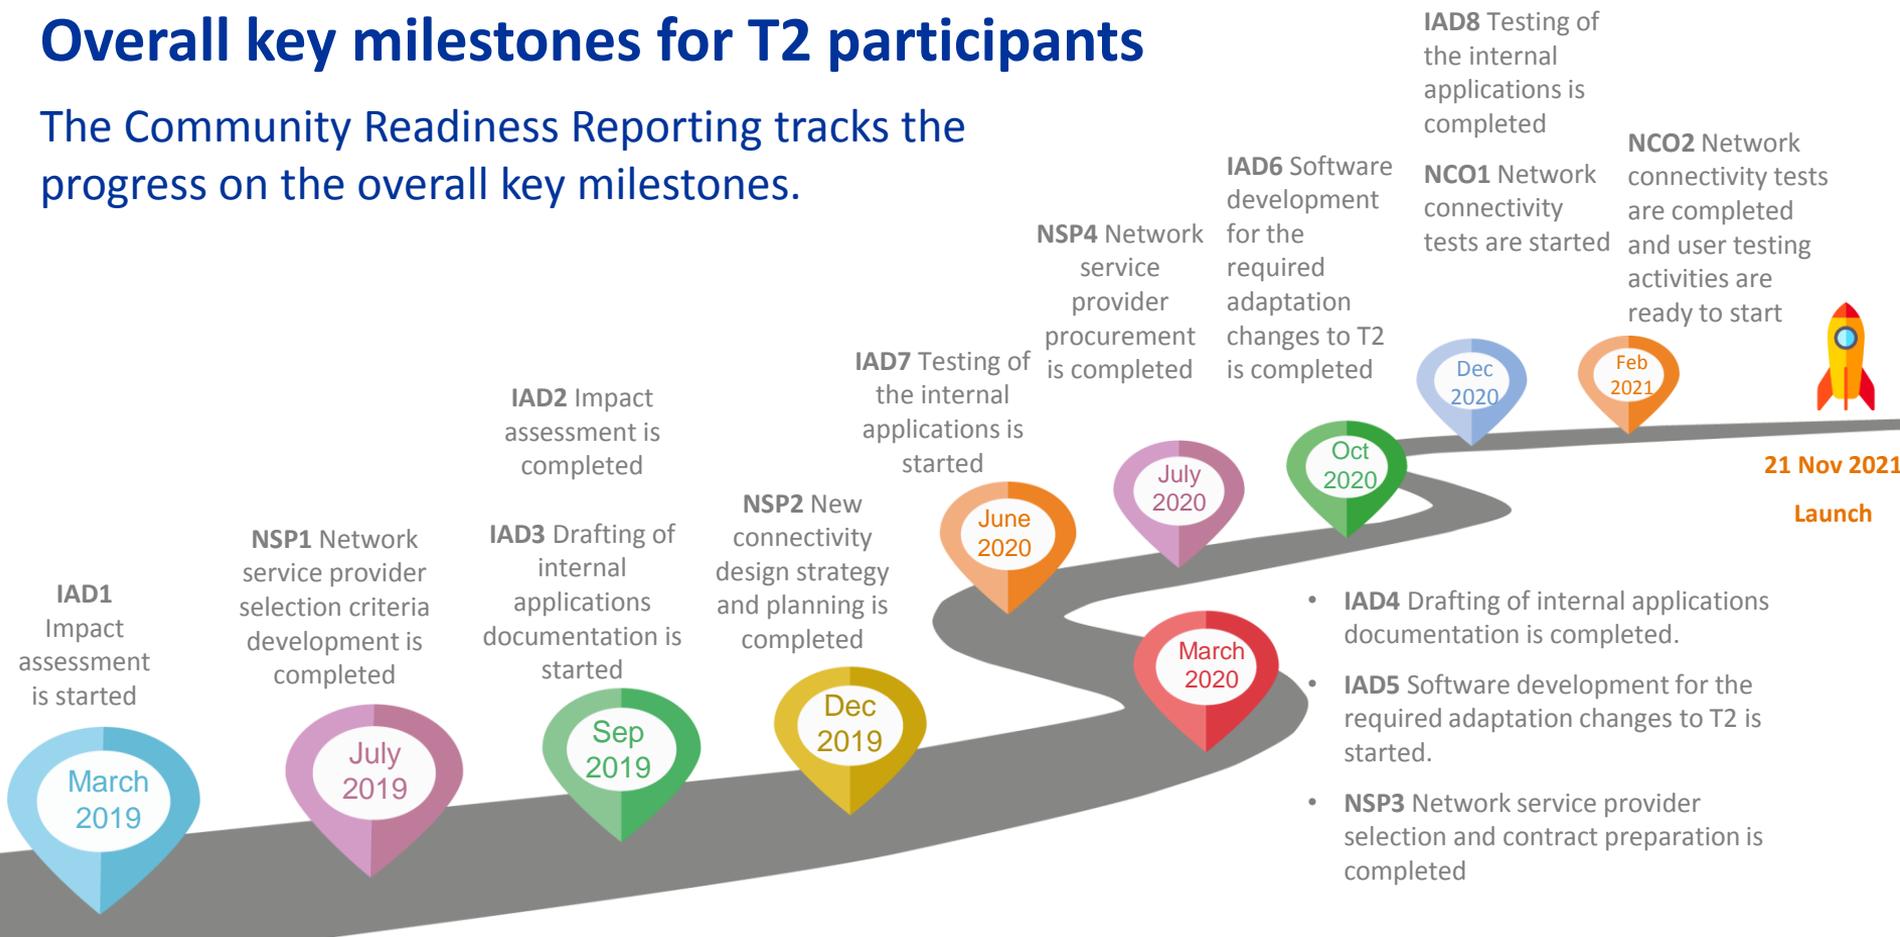

2019 Milestones

NSP1, IAD2, IAD3 reporting published on **04/12/2019**.


NSP2 reporting planned to be published **beginning of February**.

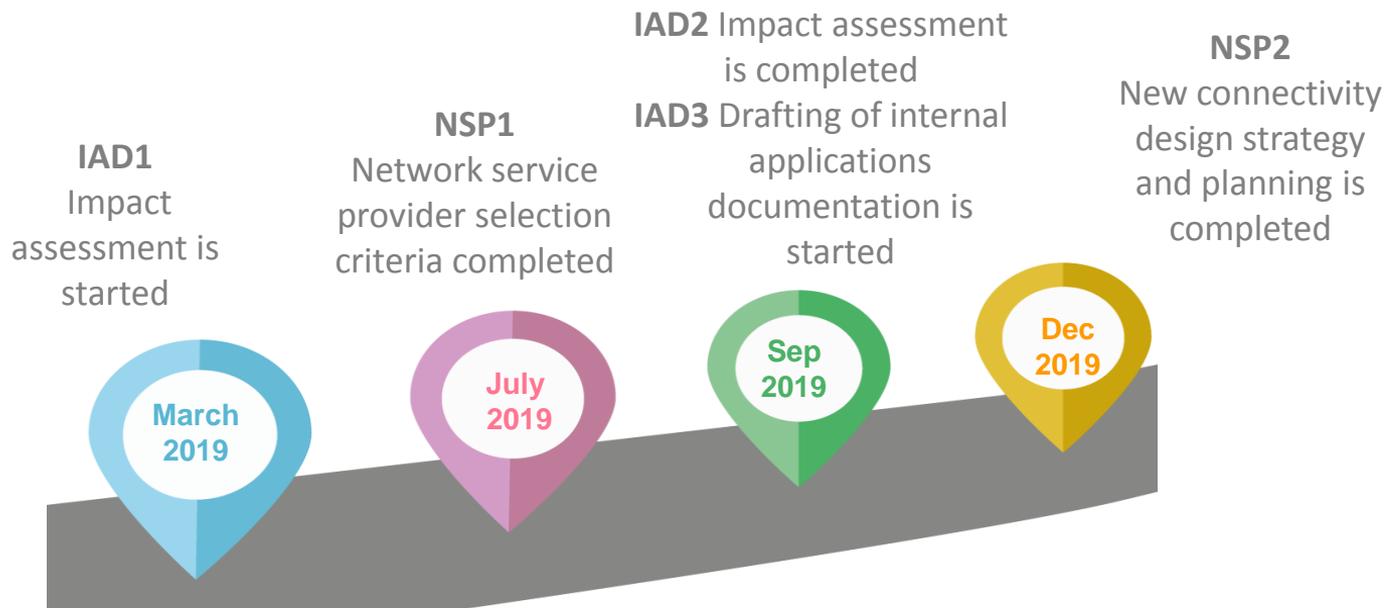

2019 - September

Impact assessment completed

Specifications started

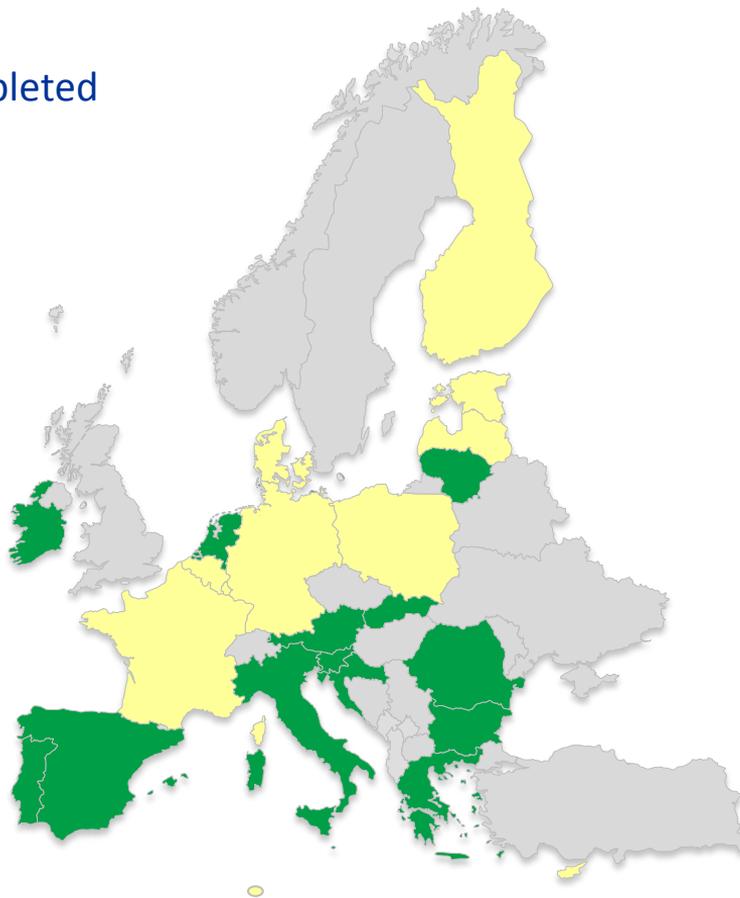

Green

Fully confident, no risk identified

Yellow

Risk identified, but can be overcome



12
Communities

13
Communities

<https://www.ecb.europa.eu/paym/initiatives/share/d/docs/c85b6-2019-12-04-joint-ami-pay-ami-seco-item-2.1.-b-community-readiness-milestones-nsp1-iad2-iad3-dashboard.pdf>

<https://www.ecb.europa.eu/paym/initiatives/share/d/docs/438a5-2019-12-04-joint-ami-pay-ami-seco-item-2.1.-b-community-readiness-report-milestones-nsp1-iad2-iad3.pdf>

2020 Milestones

- **IAD4** Drafting of internal applications documentation is completed.
- **IAD5** Software development for the required adaptation changes to T2 is started.
- **NSP3** Network service provider selection and contract preparation is completed

IAD7 Testing of the internal applications is started

NSP4 Network service provider procurement is completed


- **IAD8** Testing of the internal applications is completed
- **NCO1** Network connectivity tests are started

IAD6 Software development for the required adaptation changes to T2 is completed




*Milestone code. See: https://www.ecb.europa.eu/paym/pdf/consultations/Overall_key_milestones_to_ensure_a_successful_big-bang_migration_in_November_2021.pdf

Project timeline

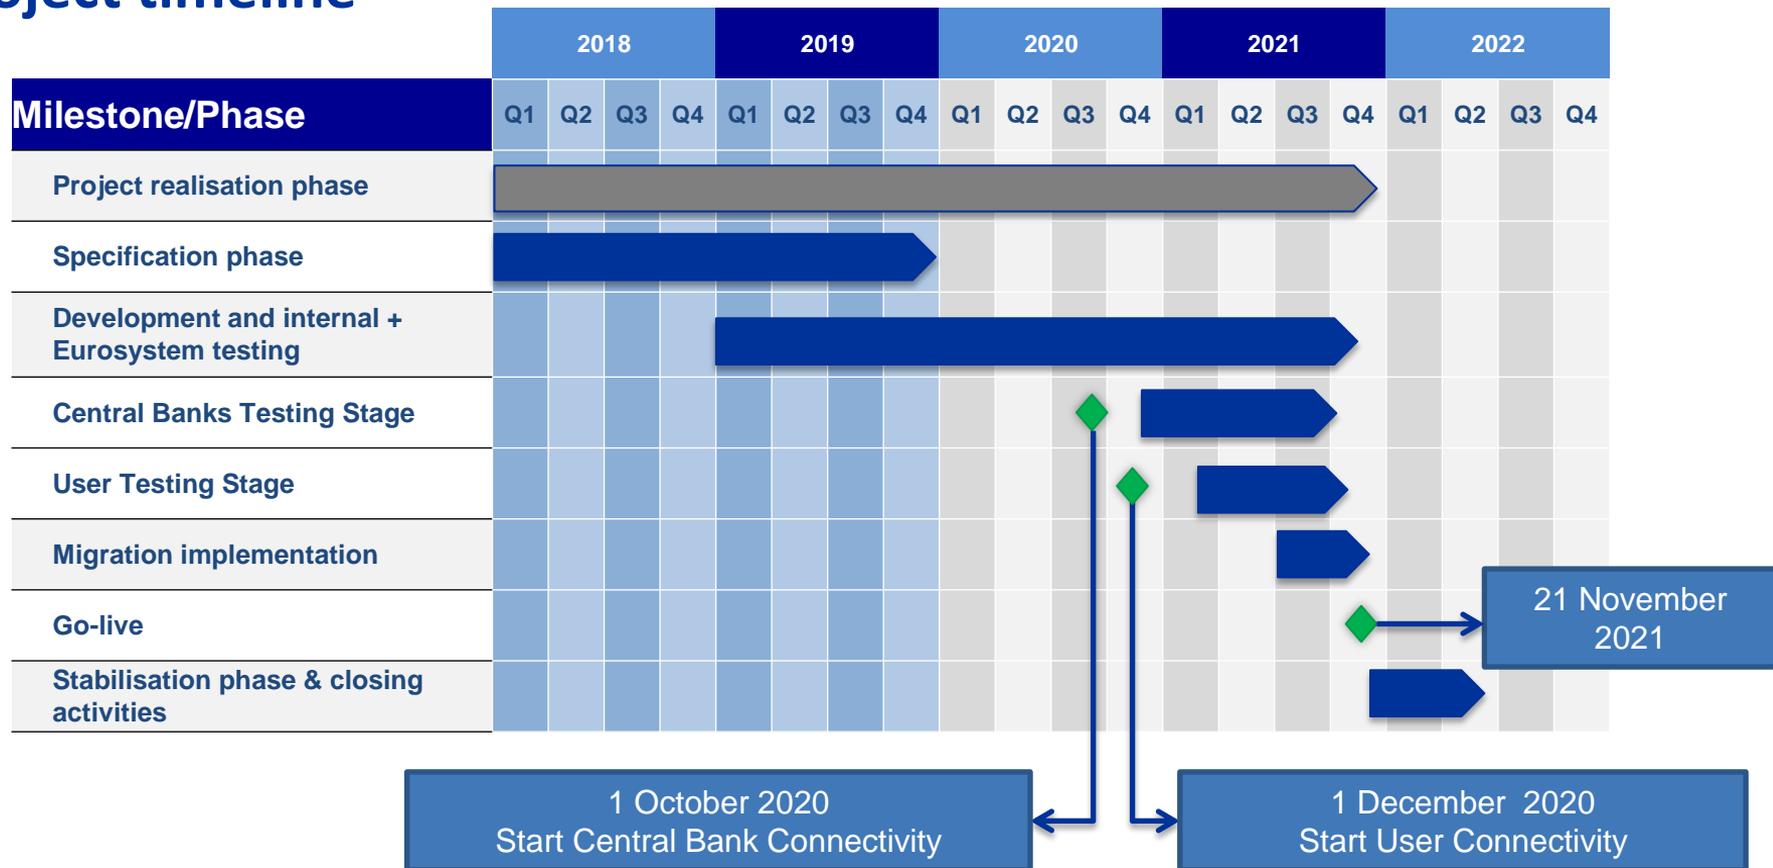

Migration Weekend (Dress) Rehearsals


Migration Weekend Rehearsal **MWR** takes place during the week during normal office hours.

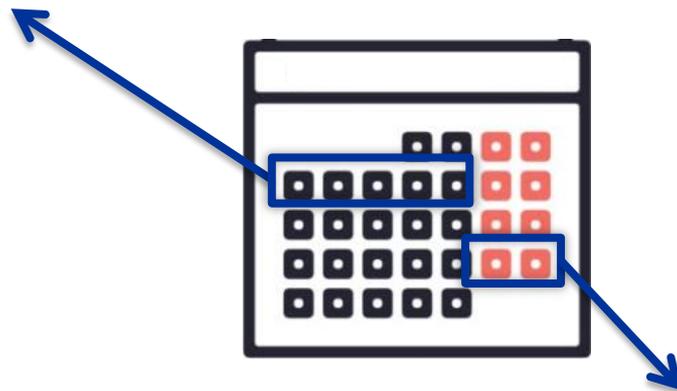

Migration Weekend Dress Rehearsal **MWDR** takes place during a weekend.

Planning

Migration Weekend (Dress) Rehearsals

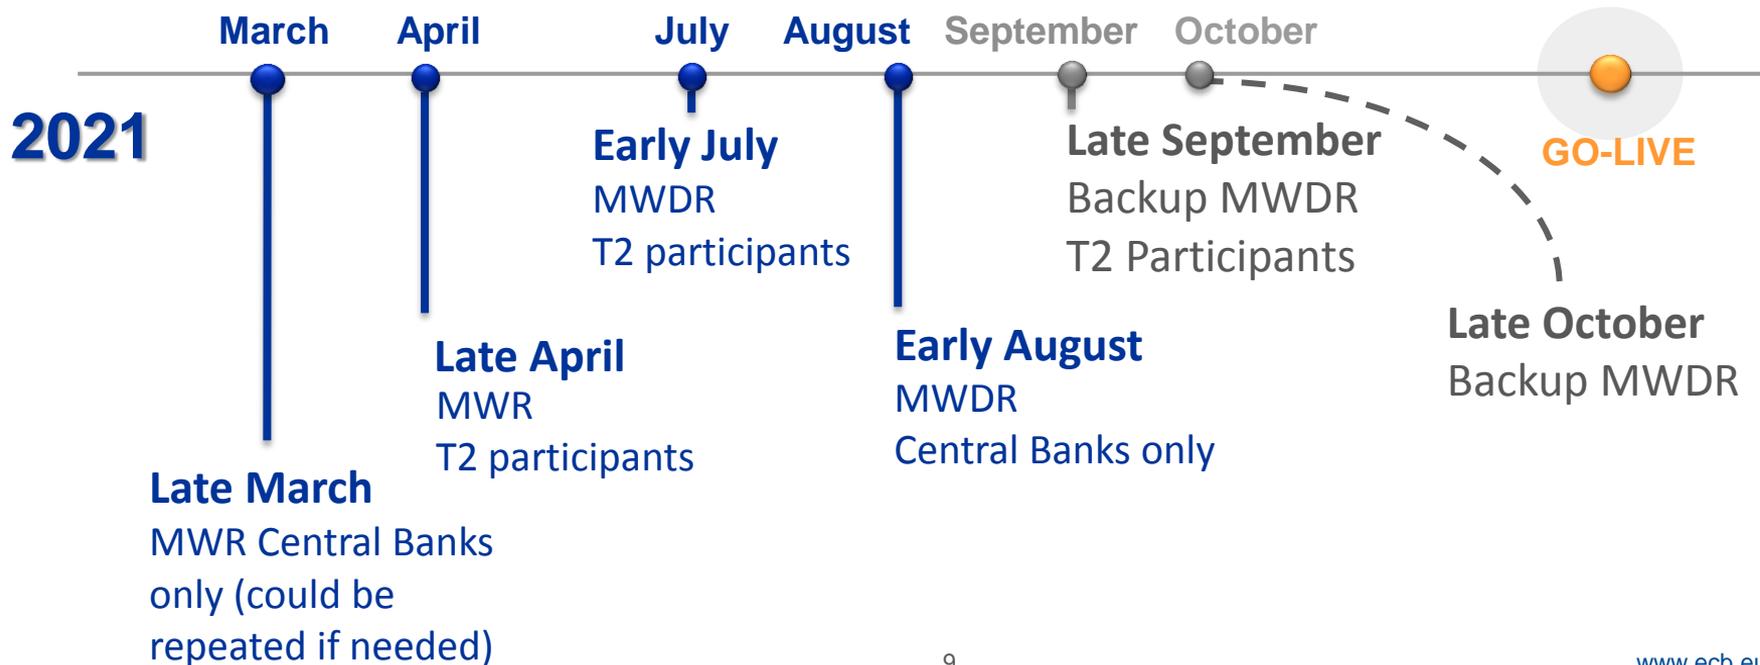

Thank you for your attention!

 **Consolidation.UT-MIG@ecb.europa.eu**

www.ecb.europa.eu/paym

 **ECB: market infrastructure and payments**
